






STEP FLOW RATE REPORT

Crosswater Holdings Ltd - Lake View House, Dartford DA1 5FU

Component data

Client :	WO110DNC	Model :	A
Category :	A	Serial number :	A
Line :	A	Test description :	BASIC FLOW RATE

Station 1

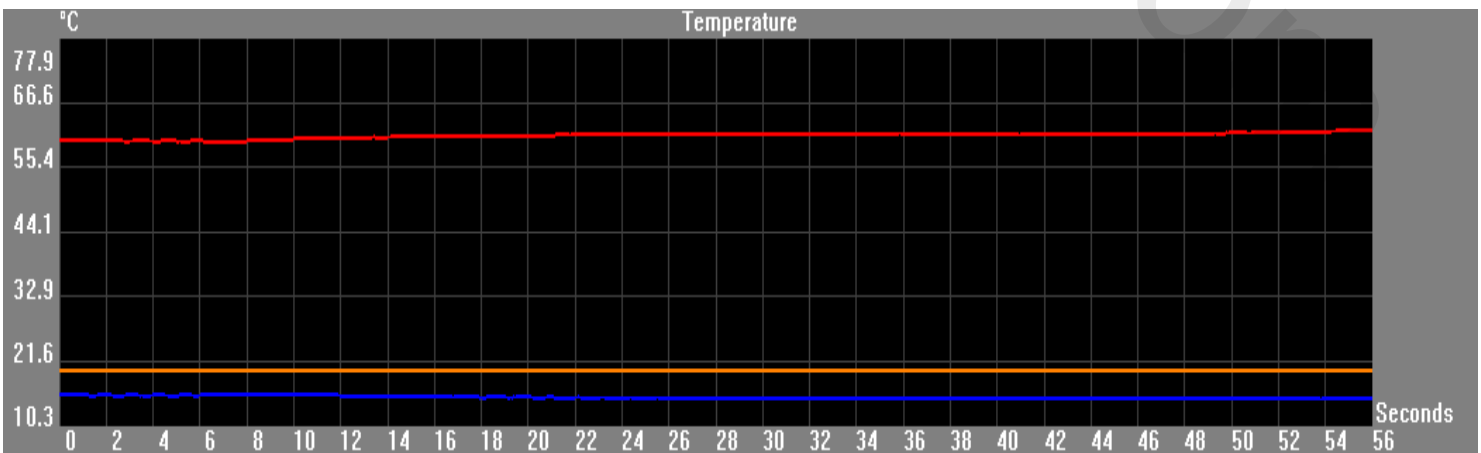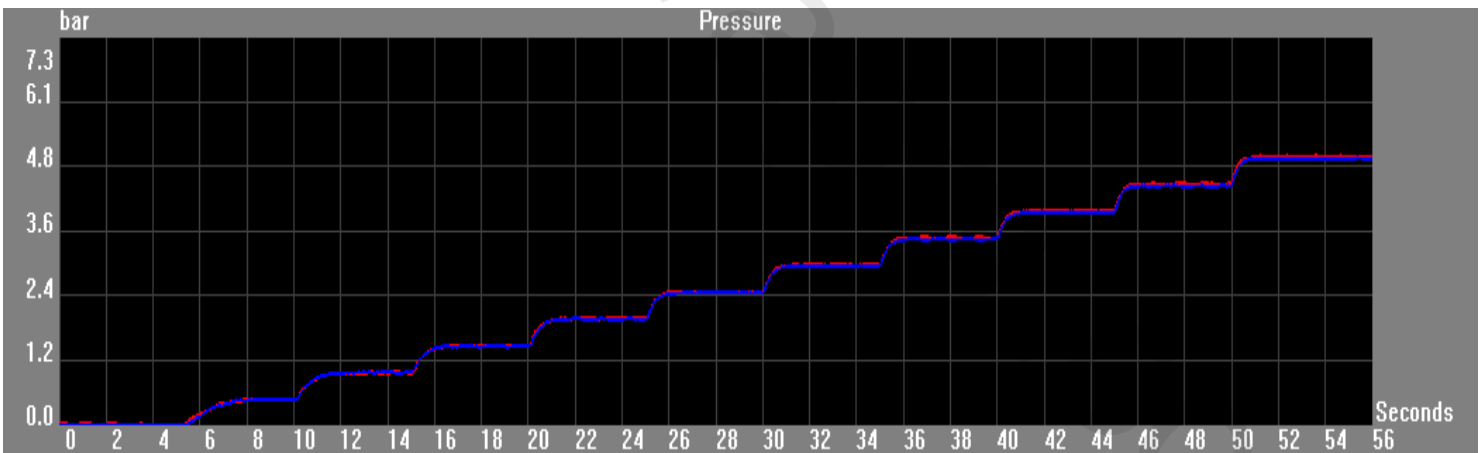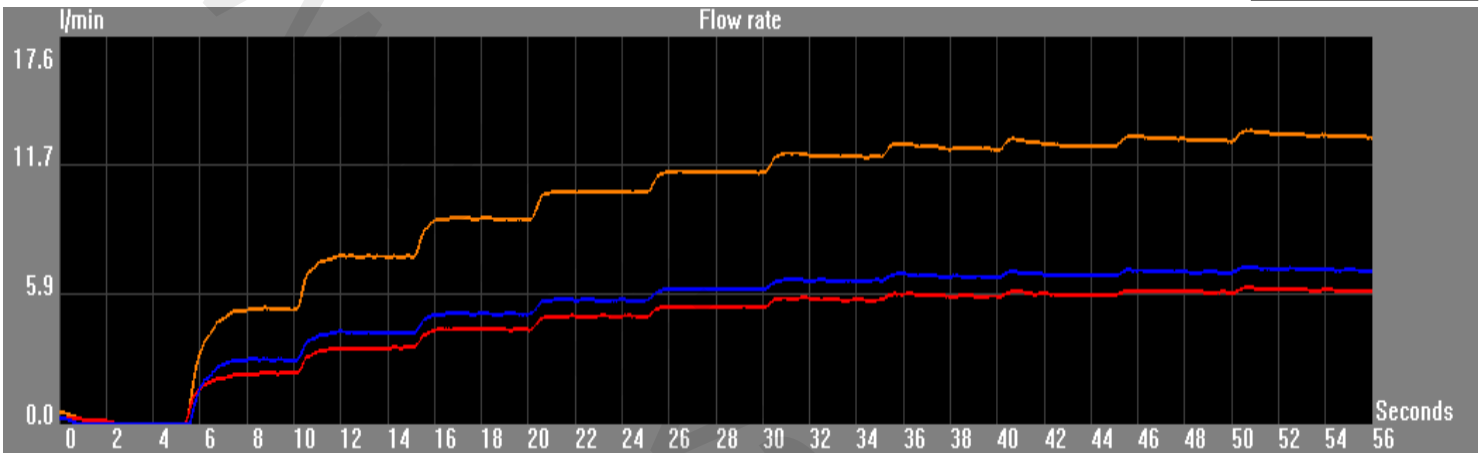

Start date :	10/03/2017 - 10:04	Operator :	Peter Memmott
Test duration :	56 (Seconds)	Signature :	_____



STEP FLOW RATE REPORT

Pag. 2/2

Crosswater Holdings Ltd - Lake View House, Dartford DA1 5FU

Component data

Client :	WO110DNC	Model :	A
Category :	A	Serial number :	A
Line :	A	Test description :	BASIC FLOW RATE

Test settings:

Station 1

Starting pressure:	0.00 bar	<input checked="" type="checkbox"/> Open hot
Step:	0.50 bar	<input type="checkbox"/> Open by-pass
Stabilisation time:	5 "	<input checked="" type="checkbox"/> Open cold
Steps number:	11	

Pitch	Hot pressure (bar)	Cold pressure (bar)	Hot flow rate (l/min)	Cold flow rate (l/min)	Mixed flow rate (l/min)	Mixed temperature (°C)
1	0.00	0.00	0.00	0.00	0.00	20.06
2	0.48	0.50	2.34	2.85	5.19	20.05
3	0.98	0.99	3.49	4.14	7.63	20.11
4	1.50	1.49	4.29	5.00	9.29	20.02
5	2.01	1.98	4.89	5.63	10.52	20.06
6	2.51	2.49	5.29	6.12	11.41	20.05
7	3.01	2.99	5.63	6.56	12.19	20.11
8	3.52	3.50	5.81	6.65	12.46	20.10
9	4.02	3.99	5.87	6.76	12.62	20.09
10	4.54	4.50	5.98	6.87	12.85	20.07
11	5.04	4.99	6.05	7.01	13.06	20.09

Notes:

Start date : 10/03/2017 - 10:04

Operator : Peter Memmott

Test duration : 56 (Seconds)

Signature : _____
